

AMENDMENT NO. 1 TO POWER PURCHASE AGREEMENT BETWEEN GEOPEAK ENERGY, LLC AND THE WESTFIELD BOARD OF EDUCATION

This amendment (“Amendment”) is entered into on this 6th day of December, 2016 by and between **GeoPeak Energy, LLC** (“Supplier”), a New Jersey limited liability company and the **Westfield Board of Education** (“Customer”), a public entity of the State of New Jersey. Throughout this Amendment, Supplier and Customer are sometimes referred to individually as “Party” and collectively as the “Parties.”

ACKNOWLEDGEMENTS:

Supplier and Customer entered into a Power Purchase Agreement (“Agreement”) dated May 12, 2016, for solar photovoltaic generated electricity to be supplied by Supplier to Customer at five (5) locations.

The Parties hereby amend the Agreement as follows:

- 1) Exhibit C attached to the Agreement is hereby replaced in its entirety as follows:**

CONSTRUCTION SCHEDULE

Updated Westfield Board of Education Solar Project Schedule (In Calendar Days)

ID	Name	Duration	Start	Finish	Notes
1	RFP Award by Westfield and Meeting	15 Days	8-Dec-15	23-Dec-15	
2	PPA Review and Execution	85 Days	15-Feb-16	10-May-16	
3	Completion of Final Permit Package, PE signed and sealed	45 Days	30-Apr-16	14-Jun-16	
4	Westfield and Its Consultant Design Review and Signoff	5 Days	14-Jun-16	19-Jun-16	BOE Engineer Approval Received 9/19/16
5	Westfield Planning Board Review and Approval	30 Days	1-Apr-16	1-May-16	Planning Board Approval Received 5/2/16
6	Utility Interconnection Review	30 Days	19-May-16	18-Jun-16	Interconnection Approval Received 6/17/16
7	NJ SRP Review	105 Days	19-May-16	1-Sep-16	SRP Approval Received 6/15/16
8	Dept of Education Review	1 Days	15-Apr-16	15-Apr-16	DOE Approvals Received In Hand 4/15/16
9	Local Permitting	31 Days	1-Jul-16	1-Aug-16	Permit Approvals Received 10/11/16
10	Pre-Construction Meeting with Westfield BOE Site Team	1 Days	4-Nov-16	4-Nov-16	
11	AC/DC Equipment and Wiring	45 Days	5-Dec-16	19-Jan-17	
12	Racking Installation	45 Days	26-Dec-16	9-Feb-17	
13	Solar Panel and Inverter Installation	60 Days	16-Jan-17	17-Mar-17	
14	System Testing and Commissioning	10 Days	18-Mar-17	28-Mar-17	
15	Township Inspections and Approvals	5 Days	29-Mar-17	3-Apr-17	
16	Substantial Completion	5 Days	4-Apr-17	9-Apr-17	
17	Utility Interconnection Approval	10 Days	10-Apr-17	20-Apr-17	The Utility normally needs only 5 days to get their work done, but may take longer and is not under Seller control
18	Commercial Operation	1 Days	21-Apr-17	21-Apr-17	This date may occur earlier if Utility completes their work earlier
19	Final Completion and Punch List Items	30 Days	22-Apr-17	22-May-17	

This schedule shall supersede any previous schedules, timelines and/or milestones. Any delays which are not under Seller's control may extend the schedule.


2) Exhibit F is hereby replaced in its entirety as follows:

EXHIBIT F

SEF PROJECT DESCRIPTIONS AND LAYOUTS


Roof mounted photovoltaic systems totaling up to 1,581.14kWp in capacity to be interconnected with the school facilities' electrical infrastructure and work synchronously with existing grid power. The systems shall be comprised of GameChange Grid-Lite racking system utilizing Canadian Solar 325w crystalline photovoltaic modules over the multiple buildings' roofs. The modules shall be connected to multiple 1000v utility grid connected string inverters.

1) Edison Intermediate School – 800 Rahway Avenue, Westfield, NJ 07090

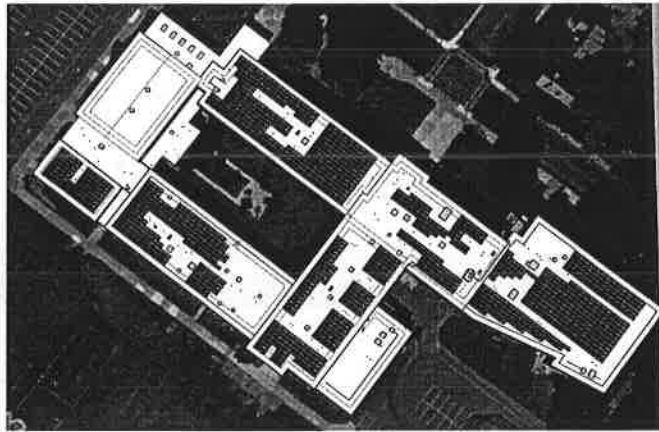


The conceptual layout above and the specifications in the RFP shall be replaced by the final engineering designs once approved by the Seller and the Board or its Consultants.

2. Roosevelt Intermediate School – 301 Clark Street, Westfield, NJ 07090

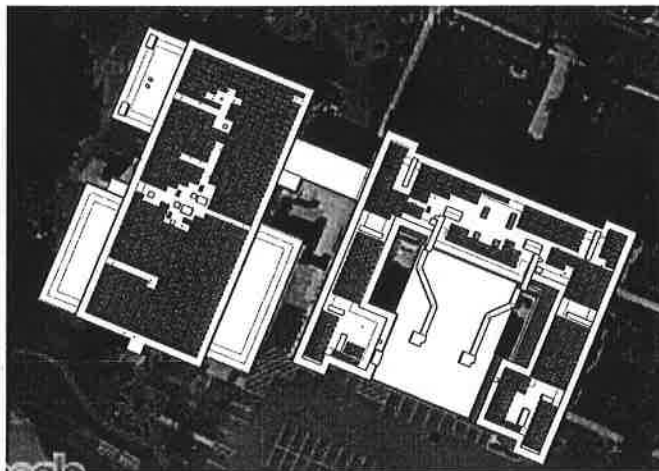


The conceptual layout above and the specifications in the RFP shall be replaced by the final engineering designs once approved by the Seller and the Board or its Consultants.

3. Tamaques Elementary School – 641 Willow Grove Road, Westfield, NJ 07090

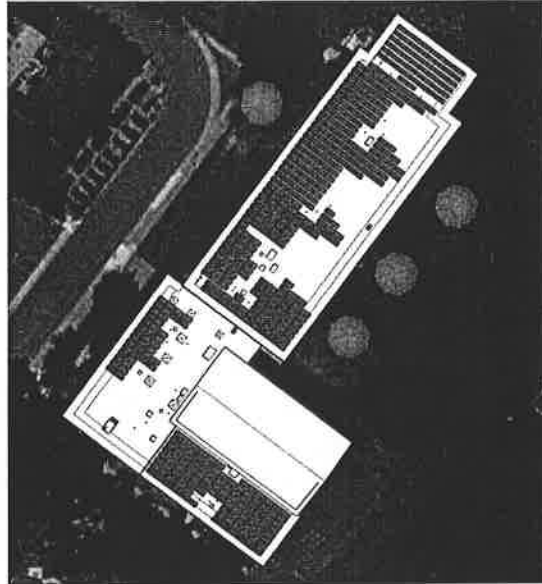


The conceptual layout above and the specifications in the RFP shall be replaced by the final engineering designs once approved by the Seller and the Board or its Consultants.

4. Westfield Senior High School – 550 Dorian Road, Westfield, NJ 07090

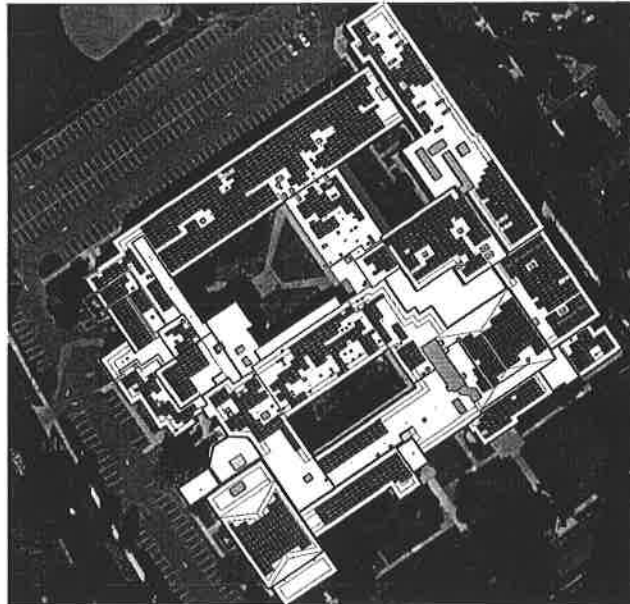

The conceptual layout above and the specifications in the RFP shall be replaced by the final engineering designs once approved by the Seller and the Board or its Consultants.

5. Wilson Elementary School – 301 Linden Avenue, Westfield, NJ 07090

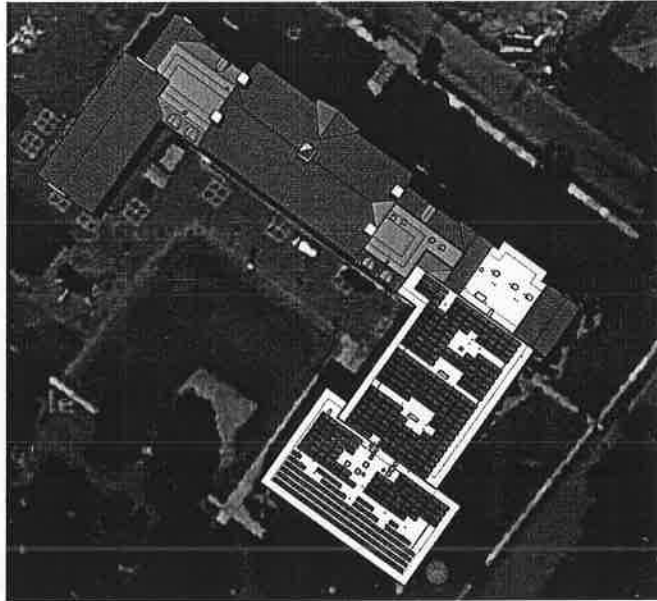

The conceptual layout above and the specifications in the RFP shall be replaced by the final engineering designs once approved by the Seller and the Board or its Consultants.

Acknowledged on behalf of GeoPeak Energy, LLC:

By: _____

Name: _____

Title: _____

By: _____

Name: _____

Title: _____

STATE OF _____)
)ss.:
COUNTY OF: _____)

On this ____ day of _____, 2016 before me personally appeared to me known as _____ of **GeoPeak Energy, LLC** and who executed the within instrument, and who acknowledged the same to be in behalf of said **GeoPeak Energy, LLC** by authority of its Board of Members and said acknowledged said instrument to be the free act and deed of **GeoPeak Energy, LLC**.

(SEAL)

Notary Public

Name
My Commission Expires: _____

